


**FY 2025 Port Grant/Bond - Monthly Update  
As of March 25, 2025**

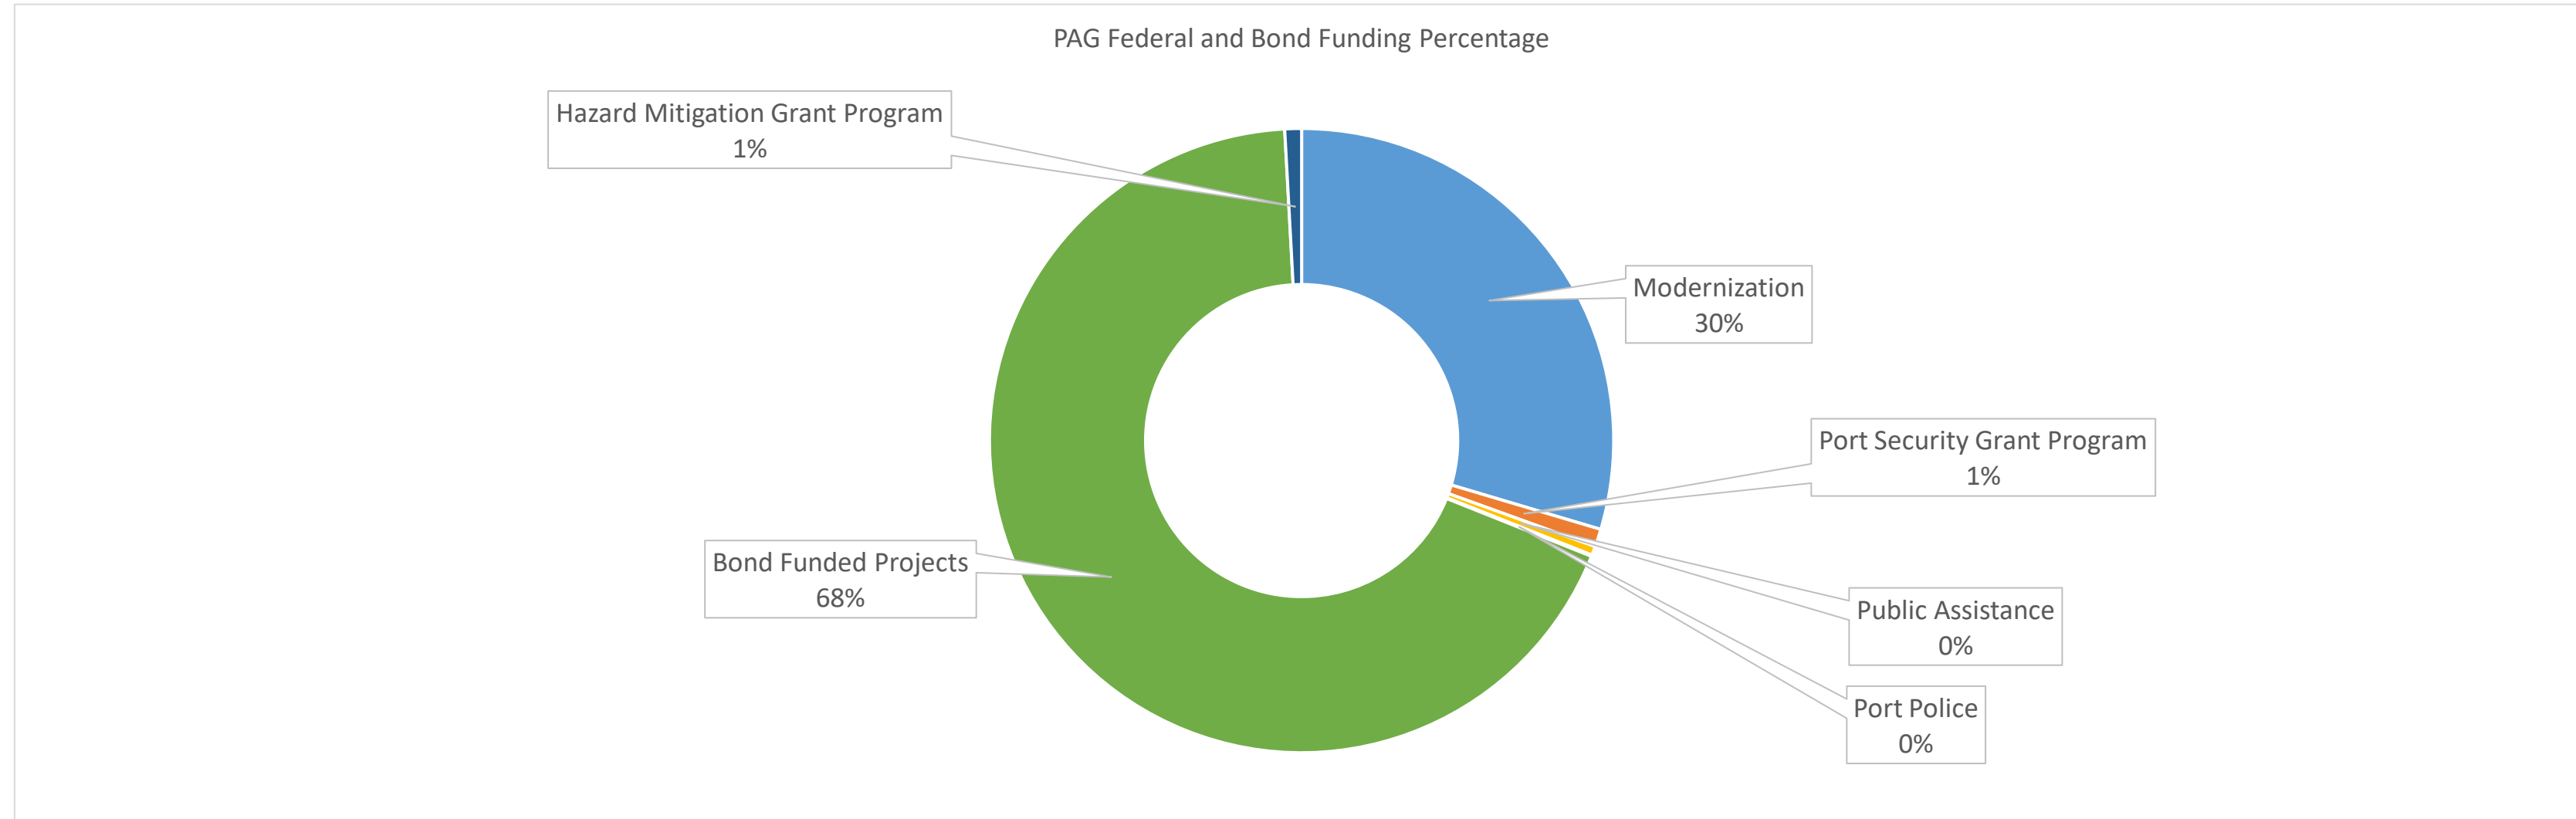

Grant Funded Projects	Total Award Amount	Total Draw Down	Total Remaining Balance	PROCUREMENT IFB/RFP/PO Number	Status
<b>Modernization</b>	<b>\$33,853,222.00</b>	<b>\$6,502,239.85</b>	<b>\$27,350,982.15</b>		
GR882-21-08 - PAG Construction Technical Oversight Services	\$1,500,000.00	\$1,462,112.43	\$37,887.57	P.O. No. 17424-OS for \$1,500,000.00	Close out report and deliverables submitted to Community Defense Liason Office. <b>NO UPDATES</b>
GR882-22-02 Growth Port Authority of Guam In-Water Infrastructure Study	\$1,200,000.00	\$1,117,713.00	\$82,287.00		<b>UPDATE:</b> All invoices have been paid and reimbursement requests submitted to the Community Defense Liason Office, along with the grant closeout report and final deliverables. Tasks were completed under budget.
GR882-23-04 Port Owner's Agent Engineer Services	\$1,450,000.00	\$1,175,132.33	\$274,867.67		Grant award notification was recieved on August 1, 2023. MOA signed by Governor - October 4, 2023; TO #14 signed by GM - January 1, 2024. The POP concluded on November 30, 2024. <b>UPDATE:</b> Deliverables and final close out report were submitted to the CDLO on February 20, 2025. Pending submission of final reimbursement request in the amount of \$269,054.77.
07-79-07614 - F1 Pier to Golf Pier Fuel Connectivity Project	\$2,413,091.00	\$0.00	\$2,413,091.00	RFP-PAG-022-003 - A&E DESIGN CONSULTING SERVICES For The Installation of a Fuel Pipeline System for F1 Pier and Golf Pier Connectivity	<b>UPDATE:</b> Amorient submitted the 100% Design Submittal; including the basis of design, drawings, and specifications on February 14, 2025. Amorient to submit pending items, to include BSP Federal Consistency Concurrence, cathodic protection stamped drawings and site certificate form. <b>Planning and Engineering Divisions met with the EDA Project Officer and Economic Development Representative (EDR) to discuss the remaining project scope and funding options moving forward. Project Officer will work with PAG on a possible amendment to grant scope and expend remaining grant funds.</b>
D20AP00136 - Phase 1: Port Authority of Guam - Welding Shop	\$240,325.00	\$91,872.90	\$148,452.10	PO No 20385OS for \$386,379.00 to Guam Evergreen Corp.	The Notice to Proceed (NTP) was issued on December 6, 2024 and commenced on December 10, 2024. Work began on January 22, 2025. <b>UPDATE:</b> Work is ongoing. Roof repairs are 85% complete and exterior spall repairs are 30% complete. The grantor also approved the PAG's request to expend federal funding prior to local funding.
D21AP10142 - Phase 2: Port Authority of Guam - Welding Shop	\$151,850.00	\$0.00	\$151,850.00		The procurement packet is being developed for the specialized welding equipment. <b>UPDATE:</b> Status Quo

**FY 2025 Port Grant/Bond - Monthly Update  
As of March 25, 2025**

Grant Funded Projects	Total Award Amount	Total Draw Down	Total Remaining Balance	PROCUREMENT IFB/RFP/PO Number	Status
D22AP00124- Generator Maintenance & Sustainment Program	\$165,375.00	\$20,291.04	\$145,083.96	PO#18867OS -1st year contract services for \$65,000.00 to Hawthorne Pacific Corp. PO#20005OS- 2nd year contract services for \$65,000.00 to Hawthorne Pacific Corp.  Generator Parts POs: PO#193080OS and PO#19311OS Landscape Management Systems Inc. \$4,314.00; PO#19310OS, PO#19313OS, PO#19315OS Far East Equipment Co. LLC. \$9,346.11; PO#19309OS, PO#19312OS, PO#19314OS Hawthorne Pacific Corp. \$11,046.35	Grant award notification was received on June 29, 2022. POP: May 19, 2022 - September 30, 2025. <b>UPDATE:</b> On Jan. 23, 2025, the PAG received approval for its no-cost extension request to September 30, 2026. This will allow the Port to fully execute Year 3 of the technical service contract. The PAG Facilities Maintenance Division has also begun the procurement for needed generator parts.
98T27101/98T34801/98T77501 - Diesel Emissions Reduction Act (DERA) - Tractor Replacement	\$676,609.00	\$376,609.00	\$300,000.00		PAG Procurement issued PO no. 20063-OS on August 27, 2024 for the purchase of two units under grant 98T77501. Delivery is anticipated within 250 days. PAG submitted final reports for grants 98T27101 and 98T34801 on October 30, 2024. An application to replace two additional terminal yard tractors was submitted under the FY2024 DERA Territory Grant on December 6, 2024. <b>UPDATE: STATUS QUO - FY 2024 Grant application status pending review by US EPA. FY2022 DERA grant no. 98T77501 - pending delivery of equipment (2 tractors), AMH (PO 20063-OS). Estimated Delivery Date: May 1, 2025</b>
MARAD AMHP - Acquisition of Specialized Container Yard Equipment	\$5,703,560.00	\$2,242,500.00	\$3,461,060.00	PO Nos. 19083/84-OS for \$2,689,408.00 and 2,205,723.00, respectively.	The Grant Agreement for MARAD FY 2022 America's Marine Highway (AMH) Grant No. 693JF72340007 was effectuated on August 4, 2023. The telescopic boom lift, reefer generators, and nine (9) terminal yard tractors are anticipated to be delivered November 2024 (boom lift) and March 2025 (generators and tractors). 180-ft telescopic boom lift was delivered November 22, 2024. On December 11, 2024, MARAD Senior Grants Management Specialist notified the PAG of its approval to purchase five 5.5-ton forklifts under the BABA waiver for Pacific Island Territories. Contract and purchase order were issued on December 13, 2024. <b>UPDATE: PO 20412-OS - PAG Maintenance Division certified the equipment to be in working condition on March 7, 2025. Planning processed the recommendation for payment on March 11, 2025; Finance subsequently processed full payment to the vendor. PO 19902-OS - PAG Transportation and Maintenance Divisions provided acceptance letter of nine (9) terminal yard tractors on March 10, 2025. Final 25% installment payment has been made to the vendor.</b>
MARAD RAISE - Wharves Service Life Extension Hardening of Wharves F1-F6	\$17,941,997.00	\$0.00	\$17,941,997.00	PAG's OAE Task Order 11, Subtask 11.9 - P.O. was issued to WSP to conduct the HABS/HAER Study mandated by State Historic Preservation Officer (SHPO).   Task Order 15 - P.O. 19948-OS was issued to WSP to conduct an Environmental Assessment. <b>Amendment approved to change period of performance from February 18, 2025 to August 18, 2025. Total billed to date \$133,151.57</b>	On August 22, 2024, the Office of the Secretary approved a no-cost scope modification request to address damages to berths F2 through F6. Before finalizing the grant agreement, pre-NEPA field surveys must be completed. To ensure project success, public scoping meetings were held with federal and local agencies to discuss the project details and benefits. On November 26, 2024, PAG requested Historic American Engineering Record (HAER) numbers for Pier F-1 and Berths F2 to F6 from the National Park Service (NPS) and is awaiting their assignment, along with feedback on the review of the HAER Mitigation Report and Photo Scans. The environmental assessment remains active, with progress guided by consultants and pre-NEPA consultations. Monthly updates are provided to Team MARAD. <b>UPDATE: The Port's OAE confirmed that the sub-consultants developed the photos in early March and have since completed the labeling and packaging process. The Port anticipates submitting the final letter to NPS by April 2025. Status: Ongoing.</b>
U.S. EPA Clean Ports Program - Net Zero Emissions Strategy Update and Implementation Plan	\$2,410,415.00	\$16,009.15	\$2,394,405.85		On Dec. 19, 2024, PAG received the Notice of Grant Award/Grant Agreement to fund the PAG Net Zero Emissions Strategy Update and Implementation Plan project.  <b>UPDATE: The draft Task Order #16 is being finalized. The PAG is scheduled to meet with the Program Office the week of the 24th to discuss progress and drawdowns on advancing approved activities, outlined in the established work plan and budget.</b>

**FY 2025 Port Grant/Bond - Monthly Update  
As of March 25, 2025**

Grant Funded Projects	Total Award Amount	Total Draw Down	Total Remaining Balance	PROCUREMENT IFB/RFP/PO Number	Status
<b>Port Security Grant Program</b>	<b>\$1,055,248.00</b>	<b>\$935,188.71</b>	<b>\$120,059.29</b>		
EMW-2021-PU-00230-S01 - Acquisition of Vessel Tracking/Radar Intrusion System	\$267,773.00	\$267,773.00	\$0.00	PO No. 187300S- G4S Security System \$347,000.00	IFB-PAG-013-22 published on August 15, 2022. Bid opening held on 10/24/2022 with one (1) submission. A budget request to utilize portion of remaining IJ #2 funding to cover any shortfall of IJ #1 was reviewed and approved FEMA on 2/4/2023. Awarded to G4S Security Systems. Project was completed on November 6, 2023 and warranty is for one (1) year up to November 6, 2024. <b>UPDATE:</b> Project Completed.
EMW-2021-PU-00230-S01 - Acquisition of Transportation Worker Identification Credentialing (TWIC) System	\$98,478.00	\$96,338.50	\$2,139.50	PO No. 182120S- ComPacific \$61,012.00 PO No. 190190S- ComPacific \$58,178.00 PO No. 178270S- DMR \$6,542.00	Award issued to ComPacific and equipment was delivered on September 29, 2022. Project Completed. A budget request to use remaining balance to purchase additional units was reviewed and approved by FEMA on 2/4/2023. On July 7, 2023 a second purchase order #190190S was cut for 6 additional TWIC handhelds and accessories as well as to cover the third year subscription service. The remaining TWIC handhelds and accessories were delivered on September 21, 2023. The remaining funds will be used to purchase a monitor to be used at Port Police's dispatch center to access the TWIC system. <b>UPDATE:</b> Procurement is currently ongoing for the monitor.
EMW-2022-PU-00149 - Acquisition of Unmanned Aerial Vehicles (UAV)	\$74,290.00	\$0.00	\$74,290.00		Revised DRAFT policy resubmitted to FEMA Program Manager on Nov. 14, 2024. Revisions made were based on FEMA's comments on first draft. This policy must be approved by FEMA prior to commencing the procurement process. Port Police re-submitted its revised UAV Policy and Procedures to FEMA for review and concurrence. Currently waiting on notification. <b>UPDATE:</b> On March 6 and March 25, 2025, follow up inquiries were sent to
EMW-2022-PU-00149 - Primary Communications Replacement of Motorola Radio Units	\$405,478.00	\$404,107.16	\$1,370.84		Grant was awarded on September 1, 2022. On July 12, 2023 Procurement issued purchase order #190230S to Motorola and Port Police recieved the units on November 28, 2023. Port Police worked with Guam Police Dept. for radio programming and is working with Finance on tagging the assets. Distribution of radio units is in progress. <b>UPDATE:</b> Radio distribution to respective individuals and as determined by Port General Manager was completed.
EMW-2022-PU-00149- Integrated Digital Enhanced Network (iDEN) Technology Redundant Interoperable Communications System Service	\$84,450.00	\$48,790.79	\$35,659.21	PO No. 18297-OS IT&E \$35,013.36 PO No. 19528-OS IT&E \$47,058.00 PO No. 201610S IT&E \$48,174.00	Grant was awarded on September 1, 2022. iDEN Services are ongoing provided by IT&E (Period of October 1, 2022 - September 30, 2023.) Third year purchase order issued for the period of October 1, 2024- September 30, 2025. <b>UPDATE:</b> Status Quo. Communication service ongoing. For FY2025 PSGP, the Port will apply to ensure continuity of service.
EMW-2023-PU-00298 - Acquisition of Two (2) Port Police Boat Trailers	\$42,003.00	\$35,751.26	\$6,251.74		Guam Home Center was awarded Purchase Order #197420S on March 19, 2024. <b>UPDATE:</b> Project Complete. Trailers have been delivered to the Port.
EMW-2023-PU-00298 - Acquisition of Port Police Durabooks and Accessories	\$43,378.00	\$43,125.00	\$253.00		MD Wholesale was awarded Purchase Order #197770S on April 1, 2024. Laptops delivered to PAG IT and are currently being configured and distributed to Port Police. <b>UPDATE:</b> Project complete.
EMW-2023-PU-00298 - Port Police Division Acquisition of Personal Protection Equipment (PPE)	\$39,398.00	\$39,303.00	\$95.00	PO NO. 202110S Code 1 Law Enforcement Equip. & Supply \$39,303.00	Notice of award - August 25, 2023. <b>UPDATE:</b> Project Complete. PPEs delivered Jan. 5, 2025
<b>Public Assistance</b>	<b>\$530,517.90</b>	<b>\$310,216.07</b>	<b>\$220,301.83</b>		
4398DR - Typhoon Mangkhut #66352	\$530,517.90	\$310,216.07	\$220,301.83		Fendering project was completed on September 30, 2022. Requested no-cost time extension for the Management & Admin. project (CAT Z) Project #99994 up to March 1, 2023. All work was completed between December 2018 through September 30, 2022. The final reimbursement payment from GHS/OCD was recieved by the PAG on October 13, 2023. <b>UPDATE:</b> Project Completed and Reimbursed.
<b>Hazard Mitigation Grant Program</b>	<b>\$989,564.00</b>	<b>\$537,824.38</b>	<b>\$451,739.62</b>		
Fendering System Hardening Project	\$603,689.00	\$151,949.38	\$451,739.62		IFB-PAG-CIP-022-008 posted on August 26, 2022. Pre-bid conference held on Sept. 7, 2022 and Site visit conducted on Sept. 9, 2022. Bid opening held on Oct. 27, 2022, 2:00 pm. Contract awarded to Cabras Marine. Notice to Proceed was given to Cabras Marine on January 10, 2023. Original project scope was 15 arch fenders and 11 cylindrical fenders. After Typhoon Mawar, a request was submitted to descope the damaged fenders from this HMGP project and add rubber arch fenders not included in original SOW. PAG received notification that FEMA approved the amendment on August 28, 2024. POP end date is May 15, 2025. <b>UPDATE:</b> Grant POP end date has been extended to November 3, 2025. Amendment No. 5 currently being reviewed by PAG legal counsel.

**FY 2025 Port Grant/Bond - Monthly Update  
As of March 25, 2025**

Grant Funded Projects	Total Award Amount	Total Draw Down	Total Remaining Balance	PROCUREMENT IFB/RFP/PO Number	Status
Warehouse 1 Hardening Project	\$385,875.00	\$385,875.00	\$0.00		IFB-PAG-CIP-022-009 posted on Sept. 13, 2022. Pre-bid conference held on Sept. 20, 2022 and Site visit scheduled for Sept. 23, 2022. Bid opening was completed on October 20, 2022. There were two (2) bid submissions received by the deadline. Both bids were opened and the documents were reviewed by the Port Staff Attorney as well as the Procurement and Engineering divisions. Meeting held on December 7, 2022 with lowest bidder to discuss submission and specifications. Awarded to IAN Corporation. Notice to Proceed was given to IAN Corp on April 16, 2023. Grant Period of Performance end date is March 18, 2024. Project date of completion is March 1, 2024 with a one (1) year warranty period through March 2, 2025. <b>UPDATE:</b> Project Complete.
<b>Port Police</b>	<b>\$80,000.00</b>	<b>\$0.00</b>	<b>\$80,000.00</b>		
PT24-03-03PPD - Operation A'dai He'Hao	\$80,000.00	\$0.00	\$80,000.00		OHS has authorized the PAG to begin grant activities. Speed enforcement activities will be scheduled as soon as possible. <b>UPDATE:</b> The PAG was able to send Port Police representatives to the 2025 Lifesavers Conference in Long Beach, CA.
<b>Bond Funded Projects</b>	<b>\$77,886,440.00</b>	<b>\$12,042,426.86</b>	<b>\$65,844,013.14</b>		
New Administration Building	\$10,445,000.00	\$0.00	\$10,445,000.00		Project is currently on hold pending Management decision. Engineering has been instructed to develop Scope of Work to repair concrete cracks and spalling and made a priority. <b>UPDATE:</b> Status Quo
Waterline Replacement and Relocation	\$6,000,000.00	\$3,763,577.30	\$2,236,422.70	PO No. 177900S for \$4,856,568.91 awarded to BME & Sons Inc.	Pipe installation along wharves F4 to F5 is ongoing. The first section of the new waterline near the fire water tank has been connected. Work has begun near the main gate to connect the new waterline and additional work that includes the installation of new fire hydrants to meet fire code standards. A change order has been conditionally approved for the new fire hydrants. <b>UPDATE:</b> Installation of the waterline has progressed to LC3. The project is estimated at 76% complete.
EQMR Building Repairs and Upgrades	\$3,628,800.00	\$2,936,123.65	\$692,676.35	PO No. 180070S for \$3,980,000.00 awarded to JJ Global Service	The repair & paint work as well as lead based paint abatement has been completed. Electrical work is ongoing. The next step is installation of the fire sprinkler system. <b>UPDATE:</b> Electrical work is 58% complete. Materials for the fire sprinkler system are now onsite.
Warehouse 1 Repairs and Upgrades	\$2,000,000.00	\$510,715.68	\$1,489,284.32	RFP No. 2019-03 - A&E Design awarded to NC Macario	The Construction IFB was published on November 25, 2024. The bid opening was held on February 5, 2025. <b>UPDATE:</b> The contract is currently pending Board approval. The next step is to appear before the PUC.
Golf Pier Repairs and Improvements	\$2,000,000.00	\$372,147.93	\$1,627,852.07	RFP No. 2019-02 - A&E design for \$484,000 awarded to NC Macario	Golf Pier was rendered inoperable after Typhoon Mawar. The PAG along with its OAE have developed cost estimates that are currently under review by FEMA. This review is ongoing. <b>UPDATE:</b> FEMA recently published the BRIC NOFO where there is a ceiling of \$2M per applicant under the State/Territory Allocation program. The other 2 programs are the Tribal States (which also has a \$2M cap) and the National Competition Program which has a cap of up to \$50M for Hazard Mitigation projects and capacity building activities.
Rehabilitation of "H" Wharf	\$46,331,895.00	\$1,740,063.86	\$44,591,831.14	PO No. 17043-OF for \$2,249,945.54 awarded to GHD Inc. New Contract Amount: \$2,656,621.37   PO No. 18140-OS was issued to Sumitomo Mitsui Construction Company, Ltd. for \$46,331,895.00	Resolution No. 2024-01 authorized the PAG GM to temporarily pause H-Wharf construction, procure additional gantry cranes, and establish comprehensive strategic measures for port operational enhancement and financial reallocation. WSP finalized the design to ensure compliance with the latest engineering codes. <b>UPDATE:</b> Status Quo
Other Priority Projects	\$4,980,745.00	\$222,668.79	\$4,758,076.21		1. Please refer to MARAD RAISE - Wharves Service Life Extension Hardening of Wharves F1-F6 for more information.  2. The TOS Upgrade scope of services is under Procurement and Legal review. <b>UPDATE:</b> Status Quo
Other Priority Projects - EnterpriseOne Financial Management System	\$2,500,000.00	\$2,497,129.65	\$2,870.35		Module updates are ongoing for vessels and SSRs. An RFP for joint comprehensive support services with GPA, GIAA, and the lead agency GWA is ongoing. The PAG is also exploring additional applications such as employee self serve and dashboards. The PAG is also exploring preventative maintenance modules and content management. <b>UPDATE:</b> Status Quo.
<b>Grand Total</b>	<b>\$114,394,991.90</b>	<b>\$20,327,895.87</b>	<b>\$94,067,096.03</b>		
